


SVV BALAJI - PROJECT GANTT CHART

Proposed baseline submitted for SVV Balaji approval. Week 1 commences 04-Aug-2026 (to be confirmed against contract start date). Red line marks the current reporting week.

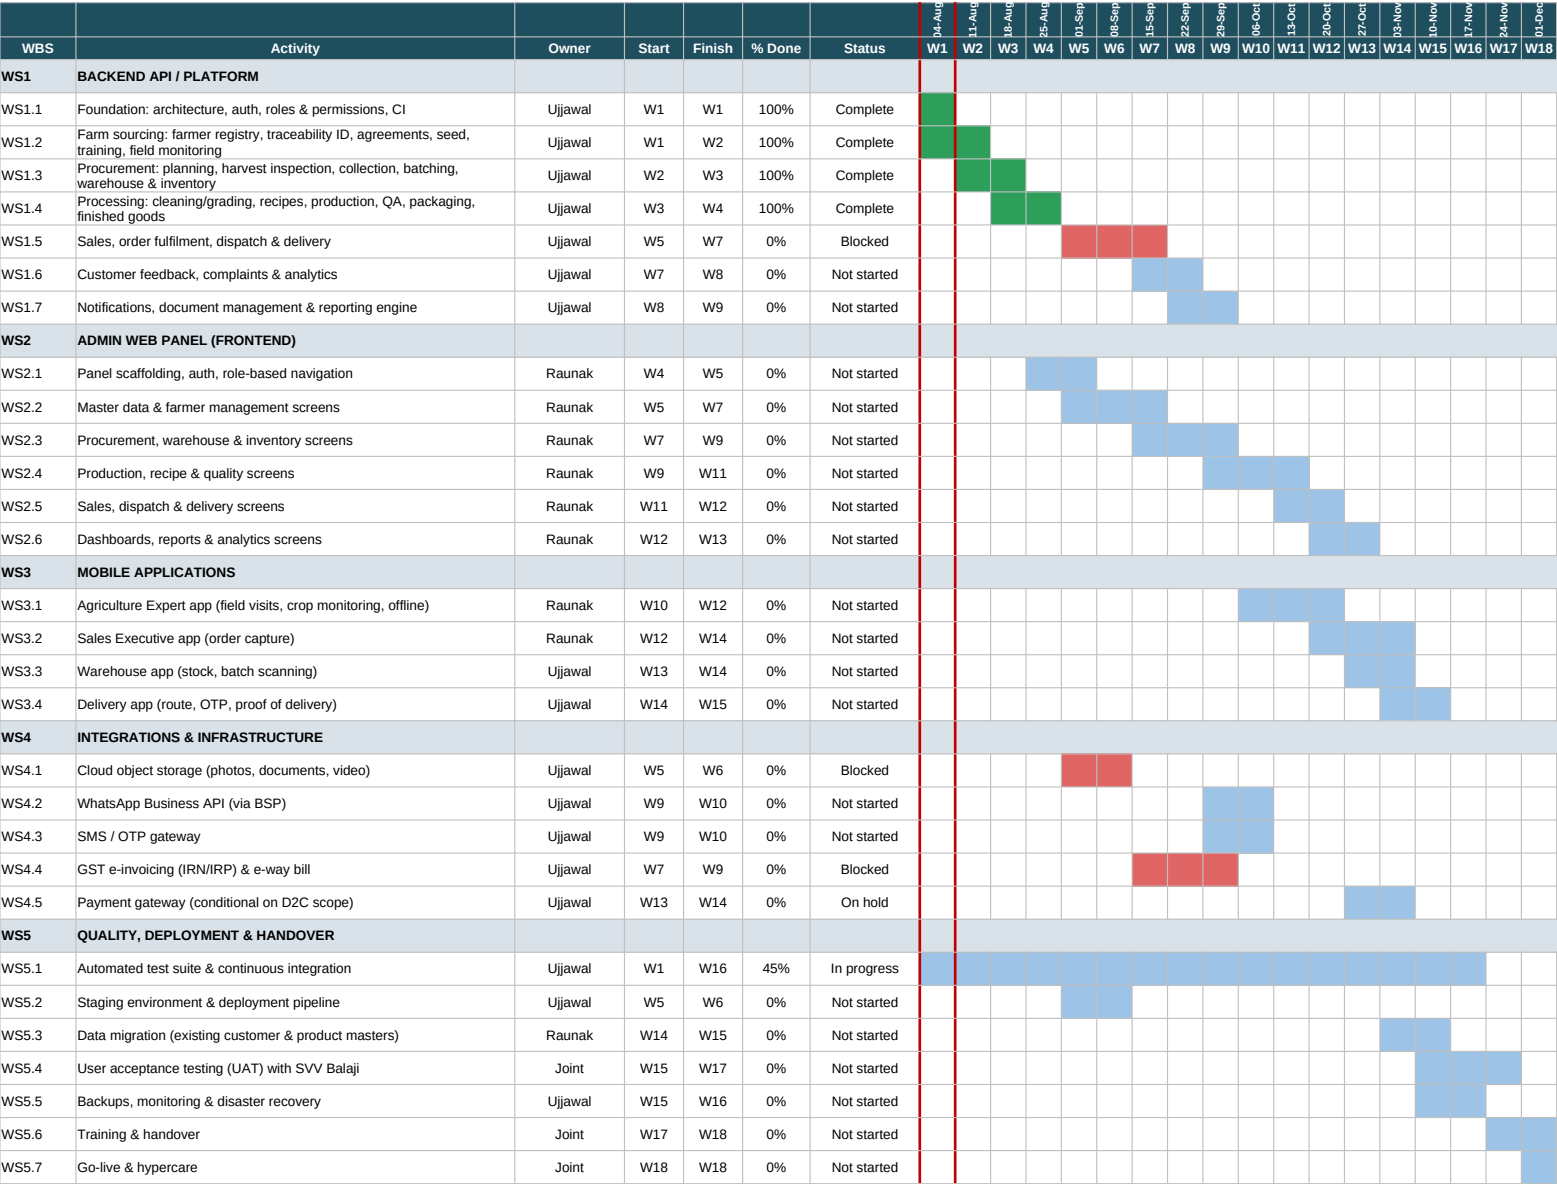

LEGEND

- Complete
- Planned / not started
- Blocked - awaiting client decision

Red vertical line = current reporting week (w/c 04-Aug-2026)
Bars are formula-driven: edit the Start / Finish week columns and the chart updates automatically.

SVV BALAJI - PROPOSED ACTIVITY-WISE SCHEDULE BASELINE

No formal Gantt baseline was approved at project commencement. This schedule is submitted for SVV Balaji approval so that all future weekly reporting can be tracked against an agreed baseline.

Dates below are PROPOSED and assume Week 1 commencing 04-Aug-2026. To be confirmed against the contract start date.

WBS	Workstream / Activity	FRD Ref	Owner	Planned Start (Wk)	Planned Finish (Wk)	Weight %	% Complete	Status
WS1	BACKEND API / PLATFORM							
WS1.1	Foundation: architecture, auth, roles & permissions, CI	FRD 5,6	Ujjawal	W1	W1	4%	100%	Complete
WS1.2	Farm sourcing: farmer registry, traceability ID, agreements, seed, training, field monitoring	FRD 7-12	Ujjawal	W1	W2	6%	100%	Complete
WS1.3	Procurement: planning, harvest inspection, collection, batching, warehouse & inventory	FRD 13-17	Ujjawal	W2	W3	6%	100%	Complete
WS1.4	Processing: cleaning/grading, recipes, production, QA, packaging, finished goods	FRD 18-23	Ujjawal	W3	W4	7%	100%	Complete
WS1.5	Sales, order fulfilment, dispatch & delivery	FRD 24-28	Ujjawal	W5	W7	6%	0%	Blocked
WS1.6	Customer feedback, complaints & analytics	FRD 31-34	Ujjawal	W7	W8	3%	0%	Not started
WS1.7	Notifications, document management & reporting engine	FRD 33-35	Ujjawal	W8	W9	3%	0%	Not started
WS2	ADMIN WEB PANEL (FRONTEND)							
WS2.1	Panel scaffolding, auth, role-based navigation	FRD 5	Raunak	W4	W5	4%	0%	Not started
WS2.2	Master data & farmer management screens	FRD 6-12	Raunak	W5	W7	5%	0%	Not started
WS2.3	Procurement, warehouse & inventory screens	FRD 13-17	Raunak	W7	W9	5%	0%	Not started
WS2.4	Production, recipe & quality screens	FRD 18-23	Raunak	W9	W11	5%	0%	Not started
WS2.5	Sales, dispatch & delivery screens	FRD 24-28	Raunak	W11	W12	3%	0%	Not started
WS2.6	Dashboards, reports & analytics screens	FRD 34	Raunak	W12	W13	3%	0%	Not started
WS3	MOBILE APPLICATIONS							
WS3.1	Agriculture Expert app (field visits, crop monitoring, offline)	FRD 12	Raunak	W10	W12	6%	0%	Not started
WS3.2	Sales Executive app (order capture)	FRD 24	Raunak	W12	W14	6%	0%	Not started
WS3.3	Warehouse app (stock, batch scanning)	FRD 16-17	Ujjawal	W13	W14	4%	0%	Not started
WS3.4	Delivery app (route, OTP, proof of delivery)	FRD 27-28	Ujjawal	W14	W15	4%	0%	Not started
WS4	INTEGRATIONS & INFRASTRUCTURE							
WS4.1	Cloud object storage (photos, documents, video)	FRD 35	Ujjawal	W5	W6	2%	0%	Blocked
WS4.2	WhatsApp Business API (via BSP)	FRD 33	Ujjawal	W9	W10	2%	0%	Not started
WS4.3	SMS / OTP gateway	FRD 28,33	Ujjawal	W9	W10	1%	0%	Not started
WS4.4	GST e-invoicing (IRN/IRP) & e-way bill	FRD 26	Ujjawal	W7	W9	1%	0%	Blocked
WS4.5	Payment gateway (conditional on D2C scope)	FRD 26	Ujjawal	W13	W14	1%	0%	On hold
WS5	QUALITY, DEPLOYMENT & HANDOVER							
WS5.1	Automated test suite & continuous integration	-	Ujjawal	W1	W16	2%	45%	In progress
WS5.2	Staging environment & deployment pipeline	-	Ujjawal	W5	W6	2%	0%	Not started
WS5.3	Data migration (existing customer & product masters)	-	Raunak	W14	W15	2%	0%	Not started
WS5.4	User acceptance testing (UAT) with SVV Balaji	-	Joint	W15	W17	3%	0%	Not started
WS5.5	Backups, monitoring & disaster recovery	-	Ujjawal	W15	W16	1%	0%	Not started

WBS	Workstream / Activity	FRD Ref	Owner	Planned Start (Wk)	Planned Finish (Wk)	Weight %	% Complete	Status
WS5.6	Training & handover	-	Joint	W17	W18	2%	0%	Not started
WS5.7	Go-live & hypercare	-	Joint	W18	W18	1%	0%	Not started
	TOTAL WEIGHTED PROJECT COMPLETION					100%	23.9%	

Weight validation (must equal 100%)

OK

Weight % reflects estimated share of total project effort and is submitted for SVV Balaji review.

Yellow cells are for SVV Balaji / Appzeto to complete. Development team: Ujjawal Mahawar and Raunak (both full-stack).

WEEKLY PROGRESS REPORT - WEEK ENDING 07-AUG-2026

WBS	Activity	Planned % (this wk)	Actual % (this wk)	Variance	Schedule Status	Evidence / Deliverable	Remarks
WS1.1	Foundation: auth, roles, permissions, CI	100%	100%	0%	On schedule	Swagger API docs; 50 automated tests passing	Complete and verified
WS1.2	Farm sourcing & farmer traceability	100%	100%	0%	Ahead of schedule	Live demo: farmer approval issues SVV-2026-NNNNNN code + QR/barcode	Complete. Traceability ID working
WS1.3	Procurement, batching, warehouse & inventory	60%	100%	+40%	Ahead of schedule	Live demo: RM-YYYYMMDD-NNN batch generation; inventory ledger	Complete ahead of plan
WS1.4	Processing, recipes, QA, packaging	0%	100%	+100%	Ahead of schedule	Live demo: full trace from finished pack to farmer	Complete ahead of plan
WS1.5	Sales, dispatch & delivery	0%	0%	0%	Blocked	-	Cannot start - awaiting Decision 1 (sales channel scope)
WS4.1	Cloud object storage	0%	0%	0%	Blocked	-	Awaiting Decision 3 (storage provider approval)
WS4.4	GST e-invoicing & e-way bill	0%	0%	0%	Blocked	-	Awaiting Decision 2 (applicability + provider)
WS5.1	Automated test suite & CI	30%	45%	+15%	Ahead of schedule	50 unit tests + 90 integration checks, all passing	Ongoing throughout project

OVERALL PROJECT COMPLETION (weighted)23.9%

Note: no activity is currently DELAYED. Three activities are BLOCKED pending SVV Balaji decisions (see sheet 3).

CONSOLIDATED ACTION TRACKER

Open actions remain on this tracker until formally closed. Ageing is calculated automatically from the date raised.

Ref	Action Item	Raised On	Responsible	Target Date	Status	Ageing (days)	Priority	Closure Remarks
A-01	Approve the activity-wise schedule baseline (Sheet 1) so future reporting has an agreed reference	07-Aug-2026	SVV Balaji	14-Aug-2026	Open	1	Critical	
A-02	Decision 1: confirm sales channel scope - B2B only, or consumer/marketplace channels also	07-Aug-2026	SVV Balaji	12-Aug-2026	Open	1	Critical	
A-03	Decision 2: confirm GST e-invoicing applicability (turnover threshold) and preferred provider	07-Aug-2026	SVV Balaji - Finance	14-Aug-2026	Open	1	Critical	
A-04	Decision 3: approve cloud object storage provider and confirm whether QR process videos are required	07-Aug-2026	SVV Balaji	14-Aug-2026	Open	1	High	
A-05	Decision 4: confirm multigrain (blended) production is in scope	07-Aug-2026	SVV Balaji	14-Aug-2026	Open	1	High	
A-06	Provide existing customer and product master data for migration planning	07-Aug-2026	SVV Balaji	28-Aug-2026	Open	1	Medium	
A-07	Nominate SVV Balaji UAT participants and confirm availability window	07-Aug-2026	SVV Balaji	28-Aug-2026	Open	1	Medium	
A-08	Confirm hosting upgrade path - current single VPS insufficient for media storage at scale	07-Aug-2026	Joint	21-Aug-2026	Open	1	High	
A-09	Set up staging environment for SVV Balaji review access	07-Aug-2026	Appzeto	21-Aug-2026	Open	1	Medium	

Open actions:

9

Critical priority open:

3

KEY RISKS, DEPENDENCIES & MITIGATION

Ref	Risk / Dependency	Impact	Likelihood	Mitigation / Corrective Action	Owner
R-01	Sales channel scope undecided (B2B vs consumer/marketplace). Order module architecture depends on it.	High	High	Decision requested by 12-Aug. Backend designed so consumer channels can be added without rework, provided scope is known before WS1.5 begins.	SVV Balaji
R-02	GST e-invoicing not in current scope. If applicable, goods cannot be dispatched compliantly at go-live.	High	Medium	Applicability to be confirmed with SVV Balaji finance team. Recommend integration via a GST Suvidha Provider.	SVV Balaji - Finance
R-03	No cloud storage provisioned. Field photos, documents and QR videos cannot be stored.	Medium	High	Provider approval requested. Current single VPS is not suitable for media at scale.	SVV Balaji
R-04	Development team is two full-stack engineers (Ojjawal, Kaunak) carrying backend, admin panel and four mobile applications. Frontend and mobile represent 45% of remaining effort and largely run in parallel from Week 9.	High	Medium	Backend APIs are complete and documented, so frontend work can proceed without waiting on further backend delivery. Sequencing has been staggered to limit concurrent workstreams. Any slippage will be reported with a revised timeline in the weekly report rather than absorbed silently.	Appzeto
R-05	Legacy customer and product master data not yet received; migration effort cannot be sized.	Medium	Medium	Sample data requested (action A-06). Import templates to be provided by Appzeto.	SVV Balaji
R-06	WhatsApp Business API costs and Meta message charges are recurring and borne by SVV Balaji.	Low	-	Confirmed and agreed in the revised SOW checklist (point 30). No further action.	SVV Balaji
